

Ministry of Finance, Economy and Policy Development
Rural Infrastructure Development Programme
2020

Ministry of Finance, Economy and Policy Development

Rural Infrastructure Development Programme

2020

01.Name of the project	: ABC Low Tension Line Fixing LED Bulb at Columbuththurai Fisheries Harbour
02.Name of the DS Division	: Jaffna
03.Name of the GN Division & GN Number	: Nedunkulam J/61
04.Name of the Implementing agency	: Ceylon Electricity Board
05.Total Allocation (Rs)	: 800,000.00
06.Total Estimate Cost (Rs)	: 843,351.60
07. Total Expenditure (Rs)	: 843,351.60
08.Name of the Contractor	: Ceylon Electricity Board
09. Date of Awarding	: 04.03.2020
10. Date of Completion	: 10.07.2020
11. Physical Progress (in%)	: 100%
12. No. of beneficiaries	: 200

Photo of before the implementation



Photo of ongoing



Photo of after the completion



Ministry of Finance, Economy and Policy Development

Rural Infrastructure Development Programme

2020

01.Name of the project	: Renovation of Aasath Cross Road 2
02.Name of the DS Division	: Jaffna
03.Name of the GN Division & GN Number	: Moor Street North J/87
04.Name of the Implementing agency	: Municipal Council, Jaffna
05.Total Allocation (Rs)	: 700,000.00
06.Total Estimate Cost (Rs)	: 700,000.00
07. Total Expenditure (Rs)	: 684,157.11
08.Name of the Contractor	: Moor Street North Rural Development Society
09. Date of Awarding	: 14.02.2020
10. Date of Completion	: 14.05.2020
11. Physical Progress (in%)	: 100%
12. No. of beneficiaries	: 100

Photo of before the implementation



Photo of ongoing



Photo of after the completion



Ministry of Finance, Economy and Policy Development

Rural Infrastructure Development Programme

2020

01.Name of the project	: ABC Low Tension Line Fixing LED Bulb at Aluppanthi Fisheries Harbour
02.Name of the DS Division	: Jaffna
03.Name of the GN Division & GN Number	: Reclamation West J/69
04.Name of the Implementing agency	: Ceylon Electricity Board
05.Total Allocation (Rs)	: 500,000.00
06.Total Estimate Cost (Rs)	: 433,942.78
07. Total Expenditure (Rs)	: 433,942.78
08.Name of the Contractor	: Ceylon Electricity Board
09. Date of Awarding	: 03.07.2020
10. Date of Completion	: 10.08.2020
11. Physical Progress (in%)	: 100%
12. No. of beneficiaries	: 1500

Photo of before the implementation



Photo of after the completion



Ministry of Finance, Economy and Policy Development
Rural Infrastructure Development Programme
2020

- 01. Name of the project : - Renovation of Kelanthoddam Internal Road
(East side) - Renovation of 4th Lane**
- 02. Name of the DS Division : - Jaffna**
- 03. Name of the GN Division & GN Number: - Nedunkulam J/61**
- 04. Name of the Implementing agency : - Municipal Council, Jaffna**
- 05. Total Allocation (Rs) :- 800,000.00**
- 06. Total Estimate Cost (Rs) : - 659,562.90**
- 07. Total Expenditure (Rs) : - 668,562.90**
- 08. Name of the Contractor : - Helanthoddam Rural Development Society**
- 09. Date of Awarding : - 15.05.2020**
- 10. Date of Completion : - 06.07.2020**
- 11. Physical Progress (in%) : - 100%**
- 12. No. of beneficiaries : - 24**

Photo of before the implementation



Photo of after the completion



Photo of ongoing



Ministry of Finance, Economy and Policy Development

Rural Infrastructure Development Programme

2020

- | | |
|--|---|
| 01. Name of the project | : - Construction of New Housing Scheme 2nd Lane |
| 02. Name of the DS Division | : - Jaffna |
| 03. Name of the GN Division & GN Number | : - Reclamation East J/68 |
| 04. Name of the Implementing agency | : - Municipal Council, Jaffna |
| 05. Total Allocation (Rs) | : - 470,000.00 |
| 06. Total Estimate Cost (Rs) | : - 462,622.27 |
| 07. Total Expenditure (Rs) | : - 462,122.47 |
| 08. Name of the Contractor | : - Reclamation East Beski Women Rural Development
Society |
| 09. Date of Awarding | : - 15.05.2020 |
| 10. Date of Completion | : - 06.07.2020 |
| 11. Physical Progress (in%) | : - 100% |
| 12. No. of beneficiaries | : - 75 |


Photo of before the implementation



Photo of ongoing



Photo of after the completion

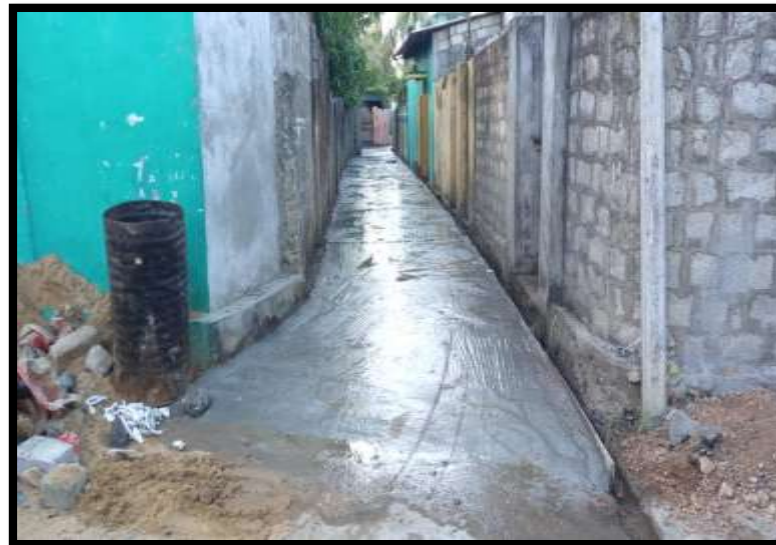

Ministry of Finance, Economy and Policy Development

Rural Infrastructure Development Programme

2020

- | | |
|--|---|
| 01. Name of the project | : - New Housing Scheme Construction of 3rd Lane |
| 02. Name of the DS Division | : - Jaffna |
| 03. Name of the GN Division & GN Number | : - Reclamation East J/68 |
| 04. Name of the Implementing agency | : - Municipal Council, Jaffna |
| 05. Total Allocation (Rs) | : - 330,000.00 |
| 06. Total Estimate Cost (Rs) | : - 284,757.16 |
| 07. Total Expenditure (Rs) | : - 321,479.87 |
| 08. Name of the Contractor | : - Reclamation East Beski Women Rural Development
Society |
| 09. Date of Awarding | : - 15.05.2020 |
| 10. Date of Completion | : - 06.07.2020 |
| 11. Physical Progress (in%) | : - 100% |
| 12. No. of beneficiaries | : - 150 |

Photo of before the implementation



Photo of ongoing



Photo of after the completion



Ministry of Finance, Economy and Policy Development

Rural Infrastructure Development Programme

2020

- | | |
|--|---|
| 01. Name of the project | : - New Housing Scheme Construction of 4th Lane |
| 02. Name of the DS Division | : - Jaffna |
| 03. Name of the GN Division & GN Number | : - Reclamation East J/68 |
| 04. Name of the Implementing agency | : - Municipal Council, Jaffna |
| 05. Total Allocation (Rs) | : - 200,000.00 |
| 06. Total Estimate Cost (Rs) | : - 174,821.86 |
| 07. Total Expenditure (Rs) | : - 196,632.34 |
| 08. Name of the Contractor | : - Reclamation East Beski Women Rural Development
Society |
| 09. Date of Awarding | : - 15.05.2020 |
| 10. Date of Completion | : - 06.07.2020 |
| 11. Physical Progress (in%) | : - 100% |
| 12. No. of beneficiaries | : - 170 |

Photo of before the implementation



Photo of ongoing



Photo of after the completion



Ministry of Finance, Economy and Policy Development

Rural Infrastructure Development Programme

2020

- | | |
|--|---|
| 01. Name of the project | : - Renovation of Navanthurai South 3rd cross Street |
| 02. Name of the DS Division | : - Jaffna |
| 03. Name of the GN Division & GN Number | : - Navanthurai J/84 |
| 04. Name of the Implementing agency | : - Municipal Council, Jaffna |
| 05. Total Allocation (Rs) | : - 1,000,000.00 |
| 06. Total Estimate Cost (Rs) | : - 435,445.75 |
| 07. Total Expenditure (Rs) | : - 435,437.90 |
| 08. Name of the Contractor | : - Navanthurai St.Nicholas Rural Fisheries Organization |
| 09. Date of Awarding | : - 18.05.2020 |
| 10. Date of Completion | : - 07.07.2020 |
| 11. Physical Progress (in%) | : - 100% |
| 12. No. of beneficiaries | : - 160 |

Photo of before the implementation



Photo of ongoing



Photo of after the completion

